



ADA•IPM

# Earned Value Management Central Repository (EVM-CR)

User Guide: Submitter

February 1, 2022

## What is the EVM-CR?

- *The EVM-CR is a data repository managed by the IPM division of OUSD(A&S) ADA, the office of Acquisition Data and Analytics.*
- *The purpose of the EVM-CR is to establish a source of authoritative Earned Value Management (EVM) and Integrated Program Management (IPM) data for the Department and to provide prompt access for PMOs, Services, OSD, and DoD Components.*




*All ACAT Programs with an EVM reporting requirement must submit to the EVM-CR*



# Getting Started

- Access Requirements & User Roles
- Creating an account
- Contract Request
- Reviewer Home

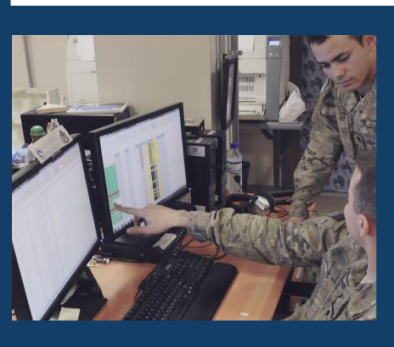

# Getting Started

## Access Requirements & User Roles

Access request via ADA IPM public website: <https://www.acq.osd.mil/asda/ae/ada/ipm/>



**ACQUISITION**  
Office of the Assistant Secretary of Defense

[Home](#)[Policy & Guidance](#)[About IPM](#)[Training](#)[EVM-CR](#)[Contact IPM](#)[ASD\(A\)](#)

ADA • Integrated Program Management

[Log In](#)[Request Account](#)[How to Register](#)

## Industry

### Submitter

RESPONSIBLE FOR  
Delivery of reports

APPROPRIATE FOR  
Industry contractors

ACCESS EVM-CR via

- External Certification Authority (**ECA**) certificate
- Certificates issued by major contractors Boeing, Northrup Grumman, Raytheon, and Lockheed Martin

### Industry Reviewer

RESPONSIBLE FOR  
Oversight of reports  
delivered by all  
submitters from their  
organization

APPROPRIATE FOR  
Industry contractors

## Government

### Reviewer

RESPONSIBLE FOR  
Reviewing, approving, and  
publishing reports

Managing submitters and  
reviewers assigned to  
efforts

APPROPRIATE FOR  
Program Office

ACCESS EVM-CR via

- Common Access Card (**CAC**)
- NDAs: Support contractors must obtain and submit NDAs in order to gain reviewer or analyst permissions

### Analyst

ALLOWED TO  
View and download  
published reports

APPROPRIATE FOR  
DoD




## Getting Started

# Registration

ADA•IPM

Access request via ADA IPM public website: <https://www.acq.osd.mil/asda/ae/ada/ipm/>



Once the user has obtained a CAC or ECA Certificate, they can **Register** for access.

- Click "Request Account"
- Create a username and password
- Fill out the User Profile

The EVM-CR Support Team will review and the request and approval typically takes 2-3 business days.

*Recommend alerting Supervisor to watch for email from EVM-CRSupport@Tecolote.com*





[Portal Home](#)

[Contact Us](#)

Signed in as Submitter | [Log Out](#) | [IPM Public Site](#)

## Profile Information

### Name

Username: Submitter

First Name

Last Name

### Service Affiliations

No service affiliations at this time.

### Personal Details

Email

Organization

MDAP/Program

DSN

Phone

Ext

253-564-1979

Phone 2

Ext

### Address

Address

Address2

City

State / Region

<Select>

Zip / Postal Code

### User Type and Security References

User Type

Citizenship

Non-Govt: Industry Data Provider

U.S. Citizen

Company Name

Supervisor Email


User Type:  
Non-Gov't Industry Provider





**Request Roles**

From the list below, choose the roles you are requesting.

 [Click here for a description of each role.](#)


EVM Roles

☐ Analyst ☐ Limited Analyst ☐ Reviewer ☒ Submitter

Add and comments about your role request here.

Submit

Select the Submitter Role





Once system access is approved, log in and select the **EVM-CR** application.





## Getting Started

# Request Contract Access

To request access to contract(s):

1. Once in EVM-CR, go to **My EVM** > **Upload Home**
2. Select the **Assigned Contracts** tab

Enter the contract number, click Send Request, and the Lead Reviewer will receive an email alerting them to the request.

Select My EVM

Department of Defense  
EVM-CR EVM Central Repository  
Acquisition Data and Analytics: IPM Division

Portal Home EVM Home **My EVM** Contact Us

**Upload Home**

Submit Effort Submission Status **Assigned Contracts** Submission History

Please enter the contract number of the request.

Contract Number  
< Contract Number >


**Send Request**

Contracts  
No assigned contracts were found



# Upload Home

- Submit
- Effort Submission Status
- Assigned Contracts
- Submission History

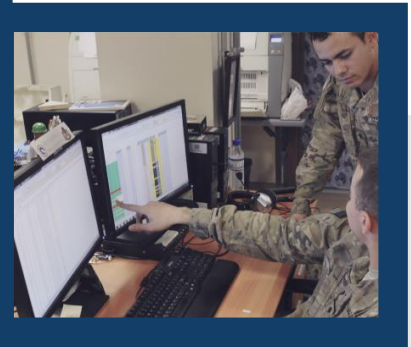

### Continue Existing Submissions

Submission ID	Program Name	Contract	Effort	File(s) Included	Report Date	Effort Start Date	Effort End Date		
14798	Jen's Program	ABCDE-00-A-0123	Delivery Order 1	Electronic Cost (IPMDAR), Human Readable Cost, Format 5	1/31/2018	7/1/2020	7/31/2025	Continue	Cancel
14796	Jen's Program	ABCDE-00-A-0123	Delivery Order 1	Electronic Cost (IPMDAR)	1/31/2018	7/1/2020	7/31/2025	Continue	Cancel

### Start New Submission on Effort

Program	Contract	Effort	Effort Start Date	Effort End Date	
Jen's Program	ABCDE-00-A-0123	Delivery Order 1	7/1/2020	7/31/2025	Start Submission
LAR Vehicle	DAAH01-03-C-0076	LAR	6/1/2016	12/30/2021	Start Submission
Vampire Countermeasure Systems	X00000-21-Y-0001	Task 1	1/1/2021	12/31/2021	Start Submission

The Submit tab is divided into two sections. Continue Existing Submissions provides a display of all submissions in the Open status; click Continue to update the submission. Start New Submission on Effort displays a list of all active assigned Efforts; click Start Submission to begin a submission.

### Submission Statuses

- **Open:** Submission has been started by the Submitter but not yet delivered to the government
- **Reviewing:** Submission has been submitted by the Submitter. 5 Day Review Period has started
- **Published:** Government has accepted the submission by pressing the Publish button or the 5 day review period has ended and the submission has auto-published and is now available for approved government Analysts to Review
- **Rejected:** Submission was Rejected by review team and is only available to Submitters and Reviewers assigned to the contract



**Upload Home**

Back

Submit

**Effort Submission Status**

Assigned Contracts

Submission History

Program	Contract	Contractor	Service	Effort	Jul-21			Aug-21			Sep-21			Oct-21		
					Cost	Schedule	CFSR	Cost	Schedule	CFSR	Cost	Schedule	CFSR	Cost	Schedule	CFSR
Jen's Program	ABCDE-00-A-0123	Dunder Mifflin	AIR FORCE	Delivery Order 1												
LAR Vehicle	DAAH01-03-C-0076	Increda Corp	ARMY	LAR												
Vampire Counter																

**Cost Details** ×

Contract: **ABCDE-00-A-0123**  
Effort Name: **Delivery Order 1**

Year: **2021**  
Month: **July**

<span style="color: red;">■</span> Cost	Legacy CPR:	Not Required & Not Delivered
<span style="color: red;">■</span> ELECTRONIC COST ON TIME	IPMR:	Not Required & Not Delivered
<span style="color: red;">■</span> ELECTRONIC COST COMPLIANCE	IPMDAR:	<span style="background-color: red; color: white;">Required &amp; Not Delivered</span>
<span style="color: green;">■</span> HUMAN READABLE COST ON TIME	Format 1:	Not Required & Not Delivered
	Format 2:	Not Required & Not Delivered
	Format 3:	Not Required & Not Delivered
	Format 4:	Not Required & Not Delivered

The Effort Submission Status tab displays a Reporting Compliance Report view of assigned contracts. This report compares required deliveries against what has been received in the EVM-CR.

- The cells are clickable and provide additional detail about the rating.



Upload Home

Back

[Submit](#) [Effort Submission Status](#) **[Assigned Contracts](#)** [Submission History](#)

Please enter the contract number of the request.

Contract Number

< Contract Number >

Send Request

#### Contracts

Contract	Effort	Program Name	Program Manager	Reporting Contractor	Reporting Contractor Division	Prime/Sub	Status	Requested Date
ABCDE-00-A-0123	Delivery Order 1	Jen's Program	Jen Horner	Dunder Mifflin	Mifflin Automotive	Prime	Assigned	
DAAH01-03-C-0076	LAR	LAR Vehicle	Debbie Buck	Increda, Corp	Division 1	Prime	Assigned	
X00000-21-Y-0001	Task 1	Vampire Countermeasure Systems	Josh Whedon	STAKE Corp	Test System	Prime	Assigned	

- The Assigned Contract tab displays all contracts assigned and provides hyperlinks to Contract Detail and Program Detail pages.
- To request access to a contract, simply enter the contract number in the field at the opt of the page and click "Send Request".



Upload Home

Back

Submit   Effort Submission Status   Assigned Contracts   **Submission History**

Enter search criteria and click 'Search'

Submission ID

<Submission ID>

Contract

<Contract>

Program

All

Submission Status

All

Report Type

All

Start Date

<Start Date>



End Date

<End Date>




Search

Clear

The Submission History tab displays all submissions for all assigned contracts regardless of status and provides filtering options to Search Submissions.

# Contract Detail

- Contract Summary
- Reviewers & Submitters
- Received Submissions
- Contract Attachments
- Reporting Stream
- Comments
- Actions
- Data Views & Charts

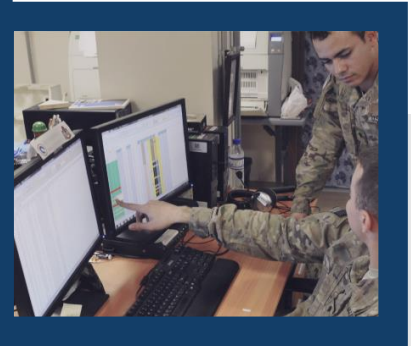



Access contract summary by clicking the Contract Number under Assigned Contracts.

Contract Detail

Back

Data Views & Charts

Program: **Jen's Program**  
Contract: **ABCDE-00-A-0123**

Reporting Contractor: **Dunder Mifflin**  
Division: **Mifflin Automotive**

Contract Type: **CPAF**  
Service: **AIR FORCE**

Contract Summary

Reviewers & Submitters

Received Submissions

Contract Attachments

Reporting Stream

Comments

Actions

	Effort	Effort Number
63	Delivery Order 1	1

DAU Gold Card Metrics (Whole Dollars)

Key Metrics	
BCWS	20,474,837,093
BCWP	20,365,245,340
ACWP	21,170,891,013
BAC	95,757,192,653
EAC (reported)	100,242,572,525
EAC (cpi)	99,545,331,054
EAC (composite)	99,967,088,422
% Schedule	21.38
% Complete	21.27
% Spent	22.11
TCPI eac	0.95

Effort	Jul-21			Aug-21			Sep-21		
	Cost	Schedule	CFSR	Cost	Schedule	CFSR	Cost	Schedule	CFSR
Delivery Order 1									

The Contract Summary Page displays all Efforts on the contract, DAU Gold Card Metrics for the most recently Published Electronic Cost Submission on the Selected Effort and a Reporting Compliance Report for all Efforts on the contract.



Contract Detail

Back

Program: **Jen's Program**

Contract: **ABCDE-00-A-0123**

Reporting Contractor: **Dunder Mifflin**

Division: **Mifflin Automotive**

Contract Type: **CPAF**

Service: **AIR FORCE**

Data Views & Charts

- Contract Summary

Reviewers & Submitters

Received Submissions

Contract Attachments

Reporting Stream

Comments

Actions
- Links

Contract Reviewers

	Reviewer Name	Organization	Role	NDA Status
	Deborah Buck	Tecolote Research	Lead Reviewer	Not Required
	Jen Horner	Tecolote Research, Inc.	Lead Reviewer	Not Required

Manage Contract Reviewers

Contract Submitters

	Submitter Name	Organization
	Jen Horner	Tecolote Research, Inc.

Manage Contract Submitters

The Reviewer & Submitters tab displays all Reviewers (by role type) and Submitters assigned to the contract.

## Contract Detail

[Back](#)

Program: **Jen's Program**  
Contract: **ABCDE-00-A-0123**

Reporting Contractor: **Dunder Mifflin**  
Division: **Mifflin Automotive**

Contract Type: **CPAF**  
Service: **AIR FORCE**

[Data Views & Charts](#)[Contract Summary](#)[Reviewers & Submitters](#)[Received Submissions](#)[Contract Attachments](#)[Reporting Stream](#)[Comments](#)[Actions ▼](#)

Submission ID	Effort	File(s) Included	Contains Admin Files	Report Date	Submission Date	Status Date	Status
14796	Delivery Order 1	Electronic Cost (IPMDAR)	No	1/31/2018	9/14/2021	9/25/2021	Published
14792	Delivery Order 1	Other, Human Readable Cost, Format 5, Executive Summary, Variance Analysis, Signature Page	No			8/10/2021	Open
14791	Delivery Order 1	Human Readable Cost, Executive Summary, Variance Analysis, Signature Page	No	8/5/2021	8/9/2021	8/15/2021	Published
14786	Delivery Order 1	Electronic Cost (IPMDAR)	No	1/31/2018	8/3/2021	8/9/2021	Published

The Received Submissions tab displays all Submissions received on the contract, associated Effort, Files provided, Report Date, Submission Date, Status and Status Date.

- **Report Date:** Contractors Accounting Close Date
- **Submission Date:** Date the Submission the Submitter submitted the Submission and status was changed from Open to Reviewing
- **Status Date:** Date Submission was set to the current Status (Open, Reviewing, Published or Rejected)

There are filtering options as well which allow the user to search by Effort, Report Type or Submission Status.



## Contract Detail

Back

Program: **Jen's Program**  
Contract: **ABCDE-00-A-0123**

Reporting Contractor: **Dunder Mifflin**  
Division: **Mifflin Automotive**

Contract Type: **CPAF**  
Service: **AIR FORCE**

Data Views & Charts

Contract Summary

Reviewers & Submitters

Received Submissions

**Contract Attachments**

Reporting Stream

Comments

Actions ▼

### CDRL Attachment

CDRLs	Effort	File Comment	Cost	Schedule	CFSR	Upload Date	Upload By
<a href="#">20201028 EVM Release Items_JH.docx</a>	Delivery Order 1		<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	10/21/2020	Jen Horner

### Other Attachment

File Name	File Comment	Upload Date	Upload By
<a href="#">banner with IPM name change.png</a>	Stop Reporting Comments	10/21/2020	Jen Horner

The Contract Attachments tab will include the contract CDRL documents (form DD-1423) as well as any communications received related to changes in reporting requirements.



## Contract Detail

Back

Program: **Jen's Program**  
Contract: **ABCDE-00-A-0123**

Reporting Contractor: **Dunder Mifflin**  
Division: **Mifflin Automotive**

Contract Type: **CPAF**  
Service: **AIR FORCE**

Data Views & Charts

Contract Summary

Reviewers & Submitters

Received Submissions

Contract Attachments

**Reporting Stream**

Comments

Actions ▾

Effort: **Delivery Order 1**      Effective Date: **7/1/2016**      Stream ID: **469**

	Effort	Effort Number	Start Date	End Date
63	Delivery Order 1	1	7/1/2020	7/31/2025

	Reporting Stream	Effective Date
63	469	7/1/2016

The Reporting Stream tab is populated at contract setup by the EVM-CR Support Team. It contains Reporting Requirements as identified in the Contract CDRL documents (form DD-1423)

This information feeds the Submitters Reporting requirements and is used to measure Reporting Compliance.

Selected DID: **IPMDAR**    IPMR    CPR/IMS

Cost	Submit Days	Submit Day Type	Frequency
Contract Performance Dataset	16	Business	Monthly

Schedule	Submit Days	Submit Day Type	Frequency
Schedule Performance Dataset	16	Business	Monthly
Native Schedule	16	Business	Monthly

Performance Narrative	Submit Days	Submit Day Type	Frequency
Executive Summary	16	Business	Monthly
Variance Analysis	16	Business	Monthly

CFSR	Submit Days	Submit Day Type	Frequency
CFSR	30	Calendar	Quarterly



Back

Data Views & Charts

Program: **Jen's Program**  
Contract: **ABCDE-00-A-0123**

Reporting Contractor: **Dunder Mifflin**  
Division: **Mifflin Automotive**

Contract Type: **CPAF**  
Service: **AIR FORCE**

Contract Summary

Reviewers & Submitters

Received Submissions

Contract Attachments

Reporting Stream

Comments

Actions ▼

The Comments tab will include comments related to the contract that are not included in Contract Attachments.

\*\* Note: This is not common.



Actions ▾

- › View IPMR Cost Data Report
- › Download IPMR Data Package
- › Download IPMR Excel Report
- › View Data Quality Issues
- › Report Data Quality Issue
- › Reporting Compliance Report

- **View IPMR Cost Data Report:** Displays all level 1 data submitted over time by Effort
- **Download IPMR Data Package:** Provides a zipped collection of Electronic Cost Data submitted over time, most recent Format 6 and Format 7
- **Download IPMR Excel Report:** Provides and Excel Export of Electronic Cost Data submitted over time
- **View Data Quality Issues:** Displays all reported Data Quality Issues and the resolution status of each
- **Report Data Quality Issue:** Provides the option to report a Data Quality Issue to the Help Desk
- **Reporting Compliance Report:** Quick link to the Reporting Compliance Report





## Contract Detail

[Back](#)

Program: **Jen's Program**  
Contract: **ABCDE-00-A-0123**

Reporting Contractor: **Dunder Mifflin**  
Division: **Mifflin Automotive**

Contract Type: **CPAF**  
Service: **AIR FORCE**

[Data Views & Charts](#)

The Data Views & Charts button will be available on contracts with efforts that have published Electronic Cost Reports.

## Data Views & Charts

[Back](#)

Program: **Jen's Program**  
Contract: **ABCDE-00-A-0123**

Reporting Contractor: **Dunder Mifflin**  
Contract Type: **CPAF**

Contract Effort:

**Delivery Order 1** ▾

Selected Period:

**1/31/2018** ▾

**Header**   WBS Elements   Summary Elements   OBS Elements   Baseline   Staffing   Charts

Header, WBS Elements, Summary Elements, OBS Elements Baseline and Staffing will display data received in published Electronic Cost files. All periods of data will be available, default display will be the most recent reporting period.



## Data Views & Charts

Back

Program: **Jen's Program**  
Contract: **ABCDE-00-A-0123**

Reporting Contractor: **Dunder Mifflin**  
Contract Type: **CPAF**

Contract Effort:

Delivery Order 1

Selected Period:

1/31/2018

Header

WBS Elements

Summary Elements

OBS Elements

Baseline

Staffing

Charts

### Performance Over Time

Element Performance Comparison

Budget Shifting

TCPI-CPI

Variance


## Chart Descriptions

- **Performance Over Time:** Chart includes key EVM Metrics as well as CPI and SPI over time
- **Element Performance Comparison:** Compares selected Elements between two time periods
- **Budget Shifting:** Displays EAC and BAC changes for select Elements
- **TCPI-CPI:** Displays TCPI EAC, CPI, CPI +10% and TCPI BAC
- **Variance:** Displays reported Cost and Schedule Variances



# Upload Submission

- File Upload
- Machine Readable vs Human Readable
- Validation Rules
- Data Quality Review
- Submission Status

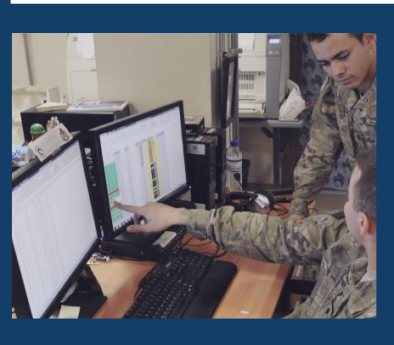

## Start New Submission on Effort

- Select the **Start Submission** option next to the appropriate Program, Contract and Effort, to begin the Submission

Upload **Home**

Back

Submit

Effort Submission Status

Assigned Contracts

Submission History

Start New Submission on Effort

Program	Contract	Effort	Effort Start Date	Effort End Date	
Jen's Program	ABCDE-00-A-0123	Delivery Order 1	7/1/2020	7/31/2025	Start Submission
LAR Vehicle	DAAH01-03-C-0076	LAR	6/1/2016	12/30/2021	Start Submission
Vampire Countermeasure Systems	X00000-21-Y-0001	Task 1	1/1/2021	12/31/2021	Start Submission

*Submitter should review Effort Start and End Dates and ensure accurate*









## Upload Submission

- Select either Cost/Schedule or CFSR Submission to continue
- Requirements table is populated based on defined Reporting Stream
- Select the icon under Upload to provide the corresponding report

**Cost / Schedule Submission**

*CFSR Submission*

### Reporting Requirements

File Type	Upload	Included
Electronic Cost (IPMR)		×
Electronic Schedule (Format 6)		×
Human Readable Cost		×
Native Schedule		×
Format 7		×
Other		

*System provides Real Time Feedback of Uploaded Requirements*



## Machine Readable Files

- JSON and UN/CEFACT files (IPMDAR CPD, SPD and IPMR Formats 1-4, 6 and 7) are read by the system and the appropriate file type will be assigned.

## Human Readable Files

- File type of PDF, Word, XLS, PPT, and Native Schedule files must be identified by submitter to receive credit for delivery

### Upload File

☒ Native Schedule

☐ Other/Human Readable

☐ Cost

☐ Format 5

☐ Executive Summary

☐ Variance Analysis

☐ Signature Page

Component

Add a comment

Submit



## System Validation Rules

- EVM-CR automatically checks machine readable files to ensure they are consistent with the IPMDAR/IPMR Data Exchange Instructions (DEI)
- Data Quality Checks include Date, Header, PMB, Order of Magnitude, Schema, Detail
  - Metrics contributing to a Data Validation Failure will be highlighted in **RED**

### Current Period

Report From: **11/23/2020**  
Report To: **12/31/2020**

### Processed Date

Processed: **2/17/2021**

### Source Data Type

Source: **IPMDAR**

### Variances

At Complete: **\$881**      Total Schedule: **\$1,629**  
Cumulative Schedule: **\$1,629**      Total Cost: **\$965**  
Cumulative Cost: **\$965**

### Report Information

Program Name: **FORGE MDPAF TTO**      Maximum WBS Level: **5**  
Phase: **FRP**      IPMR ID: **709245**  
Contract: **FA8806-20-9-0001**      Authoritative IPMR: **Yes**  
Contract Type: **CPAF**  
Contractor:  
**Raytheon Intelligence & Space**

### Performance Measurement Baseline (PMB)

MR: **\$4,994 \***      BCWP: **\$17,607**  
BAC: **\$110,933 \***      ACWP: **\$16,642**  
EAC: **\$110,052**      CPI: **1.058**  
BCWS: **\$15,978**      SPI: **1.102**

### Over Target Baseline (OTB)

OTB Date:  
BAC Adjustment:  
SV Adjustment:

CV Adjustment:  
MR Adjustment:

### Header

Dollars in

Thousands

Quantity:  
Original NCC: **\$115,963**      Contract Ceiling: **\$129,803**  
NCC: **\$115,963**      Estimated Ceiling: **\$129,803**  
CBB: **\$115,963**      Best Case EAC: **\$107,345**  
TAB: **\$115,963 \***      Worst Case EAC: **\$114,659**  
AUW:      Most Likely EAC: **\$111,519**  
Target Price: **\$129,803**  
Estimated Price: **\$125,358**

### Dates

Contract Start Date: **8/26/2020**  
Contract Definition Date: **8/26/2020**  
Planned Completion Date: **11/22/2020**  
Contract Completion Date: **8/25/2025**  
Estimated Completion Date: **8/25/2025**







## Review Data Quality Validation Report

- Display of all checks run on the file with an indication of pass/fail

## Review Performance Over Time Chart


- 5 Key EVM Metrics charted over the life of the effort. Includes indicator of where data in submitted file falls in relation to previous submissions.

### Quick Links

[Data Quality Validation](#)

[Performance Over Time](#)

Spikes or dips  
in these  
Monthly  
Metrics could  
indicate a Data  
Quality Issue

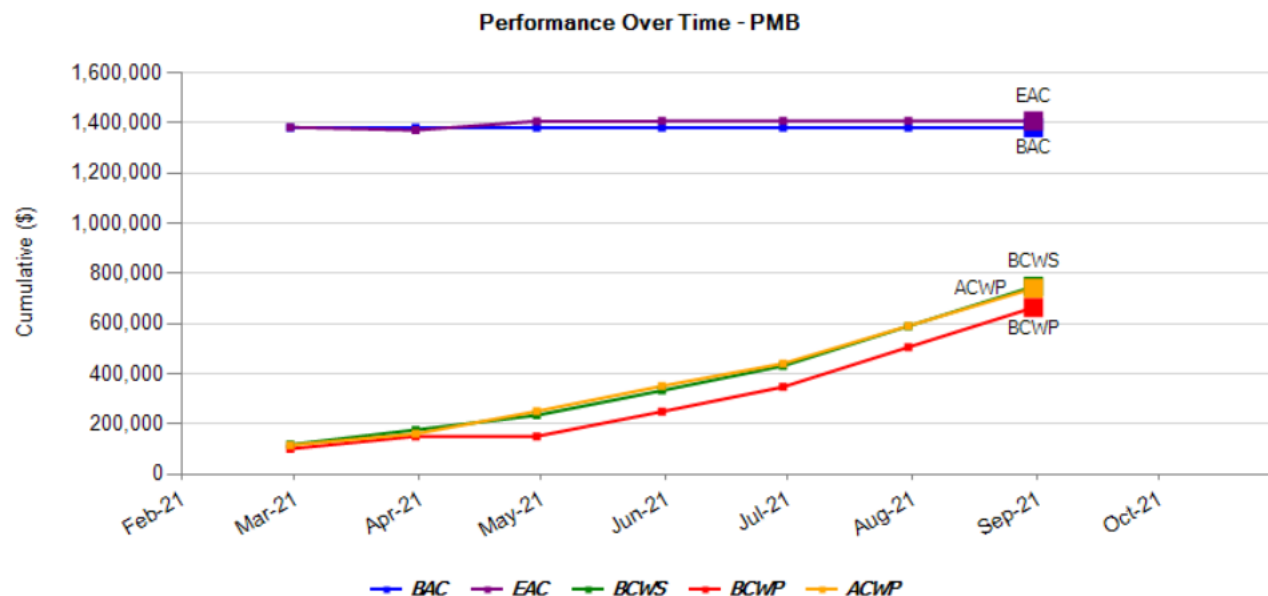

## Submission Data Validation Reports

Program: **Death Star Program (Testing Purposes)**  
Contract: **N0000-00-0001**  
Effort Name: **B-Wing**  
Report To Date: **01/31/2018**  
IPMR Id: **7221**

Download

Description	Passed	Failed
<b>EVM-CR VALIDATION RULES - DATE</b>		
Report Period From is required	X	
Report Period From must be on or before Report Period To	X	
Completion Date must be on or After Start Date	X	
Estimated Completion Date Must be on or After Start Date	X	
Planned (Budget) Completion Date must be on or after Start Date	X	
OTB Date must be on or before Report Period To (or report created date)	X	
<b>EVM-CR VALIDATION RULES - HEADER</b>		
CBB is too large (larger than 100 Billion)	X	
TAB must equal CBB unless OTB is specified	X	
Contract Ceiling price must be greater than or equal to Target Price	X	
Estimated Contract Ceiling must be greater than or equal to Estimated Price	X	
Target Price must be greater than or equal to NCC	X	
Best Case EAC must be less than or equal to Most Likely EAC	X	
Worst Case EAC must be greater than or equal to Most Likey EAC	X	
Best Case EAC must be less than or equal to Worst Case EAC	X	
Authorized Unpriced Work must equal CBB - NCC	X	
CBB must be greater than or equal to 0	X	
TAB must be greater than or equal to 0	X	





## Open

- Submission is in Submitter control, but Review team can access files and make comments

## Pending

- Submitter has submitted required files, Review team has **5 days to review** (optionally can extend to a maximum of 10 days if needed)

## Published

- Review team has completed their review and Lead Reviewer has Published the submission or review period has expired and submission has auto-published. All approved government Analysts now have access.

## Rejected

- Review team has rejected submission. Submitters and Reviewers assigned to the contract will still have access to the submission. Government Analysts will not.

*Submissions can be returned to the Open status to allow for correction or inclusion of missing files (See next slide for guidance)*



### Submission Detail

[Back](#)

Submission Status: **Reviewing** | Days To AutoPub: 5

Program: **Jen's Program**  
Contract: **ABCDE-00-A-0123**  
Effort: **Delivery Order 1**

Report Date: **1/31/2018**  
Month / Year: **January 2018**  
Submitted Date: **11/3/2021**  
Submission ID: **14792**

Contractor: **Dunder Mifflin**  
Division: **Mifflin Automotive**  
Submitter: **Jen Horner**

POC: **Jen Horner**  
Email: **jhorner@tecolote.com**  
Phone: **253-564-1979**

**Files** Data Validation Reviewers

### Reporting Requirements

Included: [Contract Performance Dataset](#), [Schedule Performance Dataset](#), [Executive Summary](#), [Variance Analysis](#)  
Missing: [Native Schedule](#)

### Submission Files

	File Name	File Type	Version	Upload Date	File Comment	Votes	My Vote
	2021_06_CPJ3_IPMR_PDF.pdf	Other	Final	8/10/2021			<input type="text"/>
	HD Tasks.xlsx	Human Readable Cost, Format 5, Executive Summary, Variance Analysis, Signature Page	Final	9/14/2021			<input type="text"/>
	Sample File.zip	Electronic Cost (IPMDAR)	Final	10/20/2021			<input type="text"/>
	Sample File.zip	Electronic Schedule (IPMDAR)	Final	10/20/2021			<input type="text"/>

### Comments

[Add Comment](#)

Date	Name	Organization	Roles	Comment	File	Actions
9/15/2021	Jen Horner	Tecolote Research, Inc.	Admin, Submitter, Reviewer	Hi Jen		
8/10/2021	Jen Horner	Tecolote Research, Inc.	Admin, Submitter, Reviewer	test		

### Submitter Actions

[Request Open Status](#)

[View Submission History](#)

To request a Submission be returned to the OPEN status, click the **"Request Open Status"** button from the Submission Detail page.

A request will be generated to the government Lead Reviewer team.



# Reports & Metrics

- Reporting Compliance
- IPMR Cost Data
- Contract Effort IPMR Cost Data
- Level 1 Portfolio



Located under **My EVM**,

**Reports & Metrics** offers a variety of reports and data views:

## Reports & Metrics

### Compliance Reports

- ⊙ **Reporting Compliance** - compares reporting requirements and reports delivered and provides a rating for each report type

### Data Views

- ⊙ **IPMR Cost Data** – grid view of all level one data delivered by effort
- ⊙ **Contract Effort IPMR Cost Data** – grid view of key metrics delivered by effort on selected program group
- ⊙ **Level 1 Portfolio** – grid view of all currently contributing contract performance data

*Only reports and data from assigned contracts will appear*

## Reporting Compliance

Back

Please choose the last time period for reporting (reports are given in a 3 month span).

- ☒ Service
- ☐ Program
- ☐ Commodity
- ☐ Contractor
- ☐ DAES Group
- ☐ ACAT

DOD

Month

November

Year

2021

Late Day Adjustment

1

Generate

The **Reporting Compliance Report** shows high-level reporting compliance scores for the selected assigned contract effort above. Compliance scores are derived by reports delivered versus what's expected following the reporting stream.



























Reporting Compliance

Compliance Details

Export

DOD

Legend

Program	Contract	Contractor	Effort		Sep-21			Oct-21			Nov-21		
					Cost	Schedule	CFSR	Cost	Schedule	CFSR	Cost	Schedule	CFSR
Death Star Program (Testing Purposes)	N0000-00-0001	Rambo Systems	AT-AT	 									
Death Star Program (Testing Purposes)	N0000-00-0001	Rambo Systems	AT-ST Walker	 									

Export

Provides an Excel Export of the Reporting Compliance Report



Pops up a comments box with who and what a person has said on the effort, contract, and program



Leads to the IPMR Cost Data table of the selected effort






Similar to the **Effort Submission Status**, each cell when selected provides additional details about each rating

Schedule Details

Contract: N0000-00-0001  
Effort Name: AT-AT

Year: 2021  
Month: October

 Schedule

 ELECTRONIC SCHEDULE ON TIME  
 ELECTRONIC SCHEDULE COMPLIANCE  
 NATIVE SCHEDULE ON TIME

Format 6 (IPMR): Not Required & Not Delivered  
IPMDAR: Not Required & Not Delivered



Reporting Compliance

Compliance Details

Export

M/Y	PROGRAM	CONTRACTOR	CONTRACT	EFFORT	ISSUE	FILE	DESCRIPTION / ACTION
SEP-21	Death Star Program (Testing Purposes)	Rambo Systems	N0000-00-0001	Y-Wing	MISSING	Electronic Cost	Not submitted
OCT-21	Death Star Program (Testing Purposes)	Rambo Systems	N0000-00-0001	Y-Wing	MISSING	Electronic Cost	Not submitted
OCT-21	Death Star Program (Testing Purposes)	Rambo Systems	N0000-00-0001	Y-Wing	MISSING	CFSR	Not submitted

The **Compliance Details** will detail in table format each red and yellow compliance issue an effort has.

- This information can also be exported to Excel



IPMR Cost Data

Back

Enter report criteria and click 'Search'

Program

Death Star

Contract

<Contract>

Submission ID

<Submission ID>

Commodity

All

Service

All

DAES Group

All

ACAT

All

Search

Clear

Hide Programs

Programs






Program Name	PNO	Contracts	With IPMR Data
Death Star Program (Testing Purposes)	0010	19	6

**IPMR Cost Data** will showcase all the level one data starting with using the selected search criteria to find specific programs


- From the selected program, review needed information for desired contract
- Click the sunglasses to check out the multiple efforts
- Click the dropdown for component names apart of each effort

Show Programs > Hide Contracts

## Contracts - Current Program: Death Star Program (Testing Purposes)

Contract	Effort	Program	Service	Reporting Contractor	Reporting Contractor Division	Prime/Sub	Submissions
123789456	Multiple (2) 	Death Star Program (Testing Purp			on Development	Prime	1
ANOTHER-TEST-CONTRACT	Task 1	Death Star Program (Testing Purp			on Development	Prime	0
N0000-00-0001	Multiple (25) 	Death Star Program (Testing Purp			on Development	Prime	138
N0000-00-0001	Task 1	Death Star Program (Testing Purp			on Development	Prime	0
N0000-00-0001	Task 1	Death Star Program (Testing Purp			on Development	Prime	0
N0000-00-0002	Multiple (3) 	Death Star Program (Testing Purp			on Development	Prime	3
N0000-00-0003	John's Deathstar	Death Star Program (Testing Purp			on Development	Prime	0
N0000-00-0003	None	Death Star Program (Testing Purp			on Development	Prime	0
N0000-00-0004	Multiple (2) 	Death Star Program (Testing Purp			on Development	Prime	1
N0000-00-0005	Multiple (2) 	Death Star Program (Testing Purp				Prime	6

1 2

**Efforts** 

Contract: N0000-00-0001

Effort Name	Effort Number
Imperial Shuttle	2
▼ A-Wing	10
▼ AT-AT	7
AT-ST Walker	5
AT-TE Walker	8
B-Wing	9
Cloud Car	21
Death Star Construction	0
Effort w/Inactive Components	7777
Hoth Snowspeeder	17

Close





- After review, click on the arrow to run a report of that particular effort
- All the data can be seen in the browser but an **Export** to an excel spreadsheet is available
- Report any data that might be an issue with **Report Data Issue**

Show Programs > Show Contracts > Hide Efforts

Efforts - Current Contract: N0000-00-0001

	Effort Name	Effort Number	Start Date	End Date	First Period	Last Per.	Run Report
✓	A-Wing	10	6/1/2019	12/31/2020	6/25/2010	5/31/2018	→
✓	AT-AT	7	3/3/2000	1/31/2025	6/23/2010	5/31/2021	→
	AT-ST Walker	5	6/1/2019	12/31/2025	6/30/2011	5/31/2018	→
	AT-TE Walker	8	6/1/2019	12/31/2020			Not Available
	B-Wing	9	6/1/2019	12/31/2020	10/25/2013	10/25/2013	→
	Cloud Car	21	6/1/2019	12/31/2020	2/27/2017	2/27/2017	→
	Effort w/Inactive Components	7777	8/1/2021	8/28/2021			Not Available
	Hoth Snowspeeder	17	6/1/2017	12/31/2020	2/28/2009	1/24/2019	→
	Imperial Shuttle	2	6/1/2019	12/31/2020			Not Available

1 2 3

Show Programs > Show Contracts > Show Efforts

Export

Report Data Issue

Program: **Death Star Program (Testing Purposes)**

Contract: **N0000-00-0001**

Effort: **A-Wing**

(Cost values are in dollars)

\*Calculated Value

Month	Year	Submission Year Month	Report From	Report To	Contract Start Date
Jun	2010	Jun-2010	5/26/2010	6/25/2010	1/1/2007
Jun	2011	Apr-2010	6/1/2011	6/30/2011	7/13/2009





Effort

A-Wing

▼

Reporting Period (Start)

6/30/2011

▼

Reporting Period (End)

6/30/2011

▼

Field(s)

BAC, EAC, etc

Attach Document *All files must be UNCLASSIFIED and less than 300 MB each*

[ no files selected ]

Browse

Issue *3,000 character limit*

Submit

Cancel

Fill out the information with details describing the data issue and hit **Submit**

## Contract Effort IPMR Cost Data

Back

Enter report criteria and click 'Generate'

Program Name

<Program Name>

Contract

<Contract>

Commodity

All



Service

All



DAES Group

All



ACAT

All



Generate

Clear

The **Contract Effort IPMR Cost Data** view shows a grid view of limited Level 1 cost metrics delivered by effort based on the selection above.

## Contract Effort IPMR Cost Data

Back

Show Search Criteria

Export

Program Name	Contract	Effort Number	Reporting Contractor Name	Contract Task Name	Effective Date	Start Date	Completion Date	Estimated Completion Date	Original NC
Death Star Program (Testing Purposes)	N0000-00-0001	33	Rambo Systems	Y-Wing	2/24/2019	2/25/2010	6/30/2021	4/30/2021	828
Death Star Program (Testing Purposes)	N0000-00-0001	7	Rambo Systems	AT-AT	5/31/2021	1/1/2021	12/31/2021	2/28/2021	1,8

The level 1 data this view provides is extensive, but selecting **Export** will provide an Excel Export. **Show Search Criteria** reveals the search box which allows you to generate the table again under any changes made.





## Level 1 Portfolio

Enter report criteria and click 'Generate'

- ☒ Calendar Year  
☐ One Year Date Range (Select Start Month/Year)

Year

2021

Generate

Clear

### Snapshot Reports

Report Name	Year	Month	Created By	Created On
ARC January 2020	2020	1	ebower	7/7/2021
ARC May 2016	2016	5	ebower	10/30/2020
ARC January 2020	2020	1	ebower	10/5/2020
ARC January 2020	2020	1	ebower	8/26/2020
ARC January 2020	2020	1	ebower	8/26/2020

1 2 3 4

View level 1 contributing contract performance data provided by two different options

- Generate a report based on selected date criteria
- Select a report from the list of snapshots

**Note: Snapshot Reports are created by OSD for specific meetings. There may be nothing available here for download.**

## Level 1 Portfolio

Show Search Criteria

Export

January 2021

Service	Program Name	Contract	Effort Name	Reporting Contractor Name	Reporting Division Name	Submission Id	Report From	Report To (Effective Date)	Contract Type (File)	Effort Name (File)	Program Phase	Start Date	Definitization Date	Co Da
DOD	Death Star Program (Testing Purposes)	N0000-00-0001	AT-AT	Rambo Systems	Awesome Weapon Development	16879	5/1/2021	5/31/2021	CPFF	VCS Development	Development	1/1/2021	1/1/2021	12/

Like previous level 1 data reports, there is an option to export results to an Excel spreadsheet.

